

## Floating Bridge and Landings construction activities



Crews are making progress installing electrical components for the new SR 520 floating bridge. Once complete, the new bridge will have over 300 miles of electrical wiring that will help maintenance crews to monitor each of the 77 pontoons that support the new floating bridge. Photo taken: Oct. 27



The new 14-foot-wide bike and pedestrian path continues to take shape as new railing is installed on the north side of the new floating bridge. Photo taken: Oct. 22

**Americans with Disabilities Act (ADA) information:** This material can be made available in an alternate format by emailing the WSDOT Diversity/ADA Affairs team at [wsdotada@wsdot.wa.gov](mailto:wsdotada@wsdot.wa.gov) or by calling toll free, 855-362-4ADA(4232). Persons who are deaf or hard of hearing may make a request by calling the Washington State Relay at 711.

**Title VI Notice to Public:** It is the Washington State Department of Transportation's (WSDOT) policy to assure that no person shall, on the grounds of race, color, national origin or sex, as provided by Title VI of the Civil Rights Act of 1964, be excluded from participation in, be funded programs and activities. Any person who believes his/her Title VI protection has been violated, may file a complaint with WSDOT's Office of Equal Opportunity (OEO). For additional information regarding Title VI complaint procedures and/or information regarding our non-discrimination obligations, please contact OEO's Title VI Coordinators, or Jonté Robinson at (360) 705-7082.

Visit us online: <http://bit.ly/520Flickr>

## SR 520 construction update: October 2015

### Floating Bridge and Landings construction activities



Crews pour concrete at the west end of the new floating bridge to complete its final section of roadway. Photo taken: Oct. 22




Crews smooth newly poured concrete to complete the final section of roadway for the floating bridge. Photo taken: Oct. 22


**West Approach Bridge North construction activities**



Crews pour concrete into steel forms to create the first two support columns for the West Approach Bridge North. Photo taken: Oct. 14

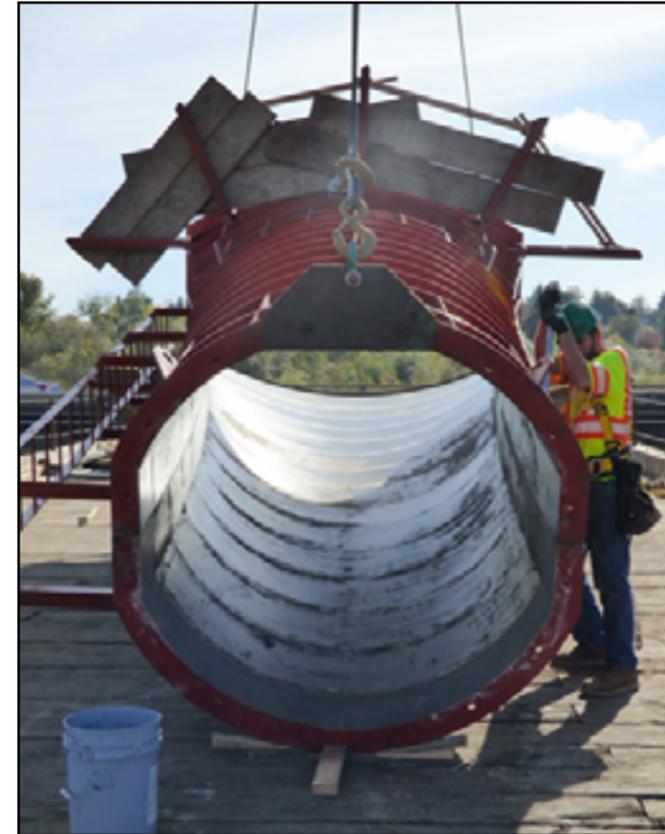


Side view of the mold used to form concrete columns for the WABN. Photo taken: Oct. 30

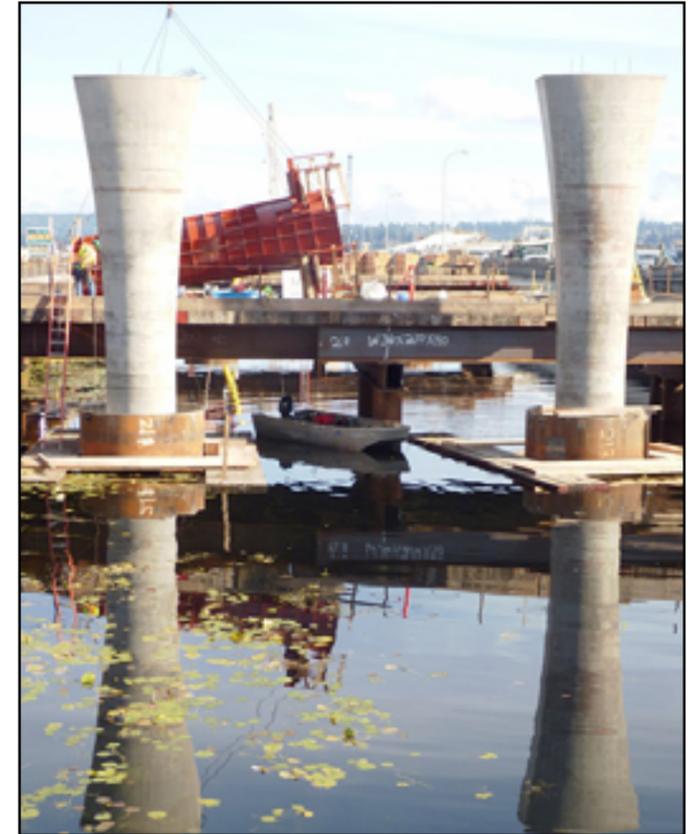

Concrete columns for the new west approach bridge stand exposed after their molds were removed. Photo taken: Oct. 30



New King County Metro bus shelters are up and running on Montlake Boulevard East, just north of East Lake Washington Boulevard. Photo taken: Oct. 16

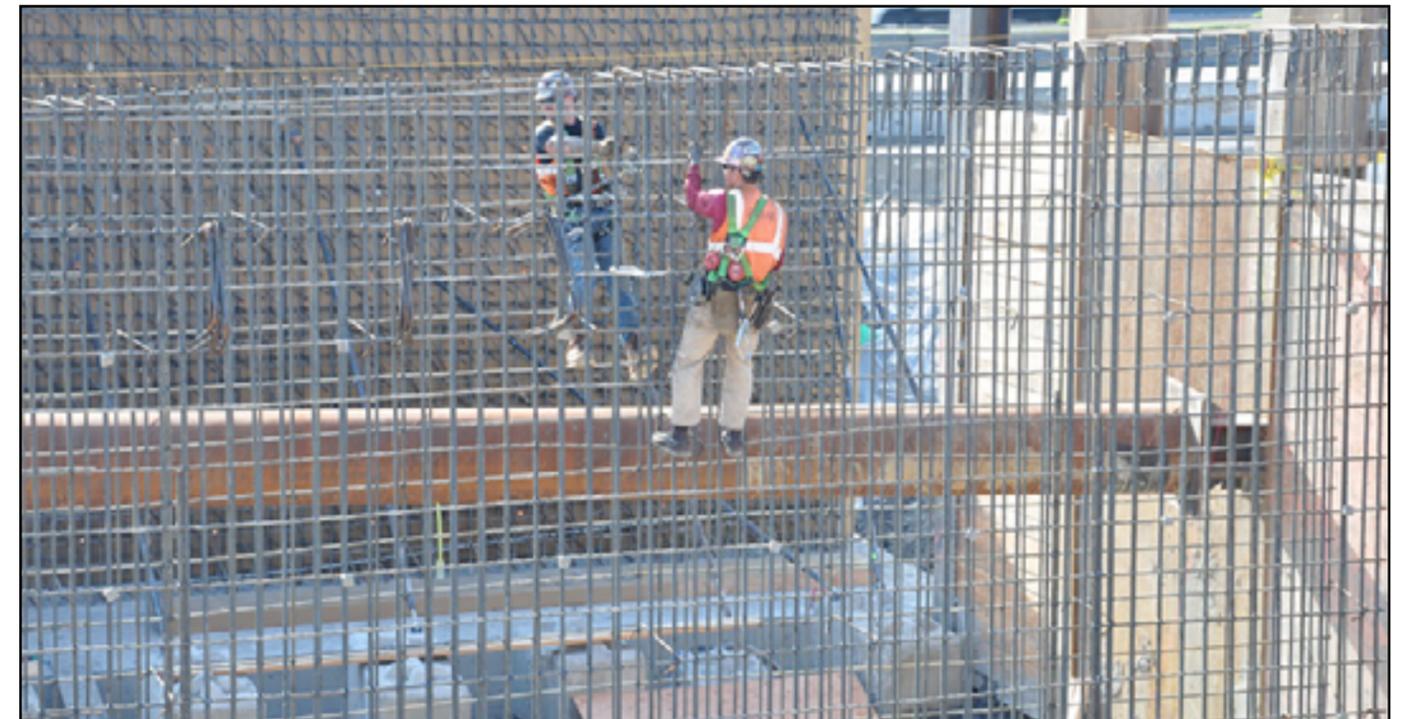

Crews tie rebar for construction of a new SR 520 westbound off-ramp at 24th Avenue East in Montlake. Photo taken: Oct. 16
