




**Floating bridge construction - Lake Washington**

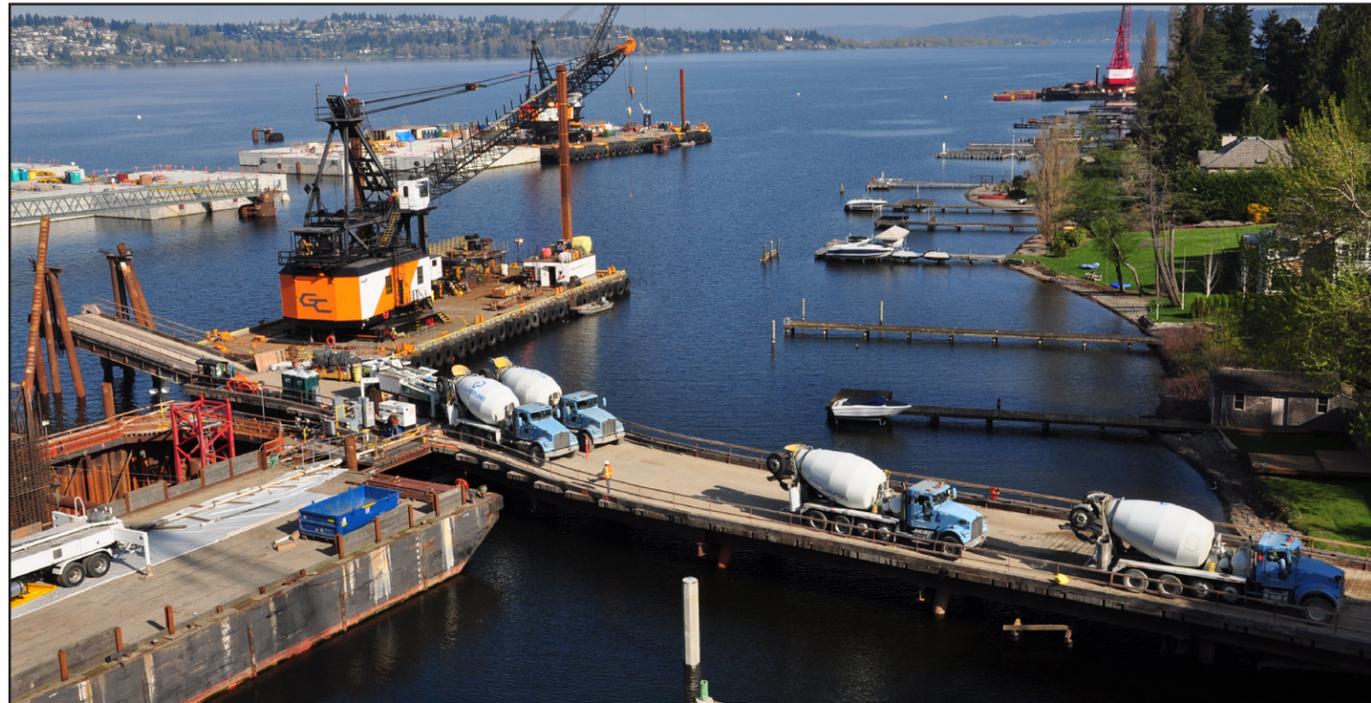

Crews use trucks to deliver concrete for new east approach pier construction on Lake Washington near the Medina shoreline.

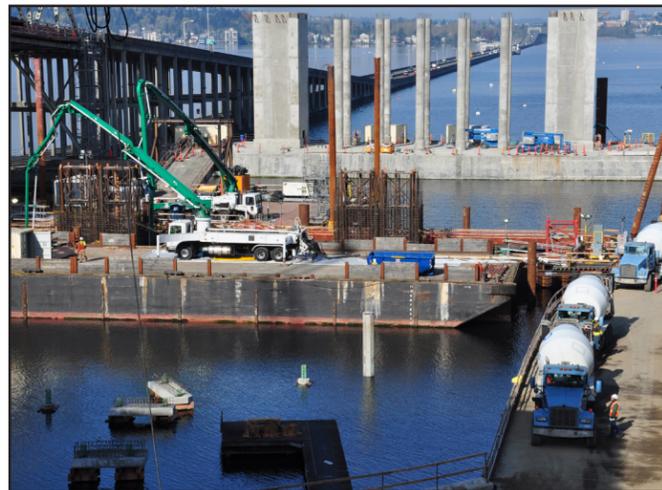

View looking east towards construction of the new east approach structure near the Medina shoreline. Crews pour concrete to form new pier structures.

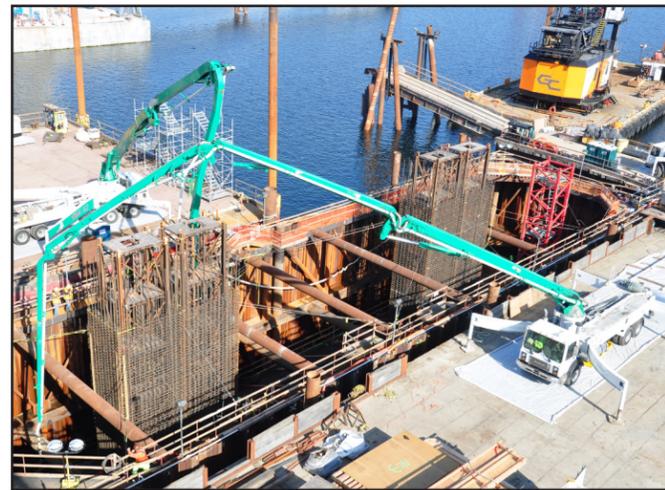

Crews use a stabilized truck and heavy machinery to pour concrete into forms for new east approach pier structures near the Medina shoreline.

**Americans with Disabilities Act (ADA) Information:** This material can be made available in an alternate format by emailing the WSDOT Diversity/ADA Affairs team at [wsdotada@wsdot.wa.gov](mailto:wsdotada@wsdot.wa.gov) or by calling toll free, 855-362-4ADA(4232). Persons who are deaf or hard of hearing may make a request by calling the Washington State Relay at 711.

**Title VI Notice to Public:** It is the Washington State Department of Transportation's (WSDOT) policy to assure that no person shall, on the grounds of race, color, national origin or sex, as provided by Title VI of the Civil Rights Act of 1964, be excluded from participation in, be denied the benefits of, or be otherwise discriminated against under any of its federally funded programs and activities. Any person who believes his/her Title VI protection has been violated, may file a complaint with WSDOT's Office of Equal Opportunity (OEO). For additional information regarding Title VI complaint procedures and/or information regarding our non-discrimination obligations, please contact OEO's Title VI Coordinators, George Laue at (509) 324-6018 or Jonte' Sulton at (360) 705-7082.

Visit us online: [wsdot.wa.gov/projects/SR520Bridge](http://wsdot.wa.gov/projects/SR520Bridge)

**SR 520 construction update: April 2013**

**Eastside construction**



View of construction and paving activities during the April 19-22 Eastside closure, looking west towards 84th Avenue Northeast.



Crews complete work on girders for the new Bellevue Way overpass along SR 520 during the April 19-22 Eastside closure.



Crews carry old asphalt sections of roadway to an excavator for removal just east of the Bellevue Way overpass along SR 520 in April 2013.


## Pontoon construction - Aberdeen



View of a new Cycle 2 pontoon near completion in the Aberdeen casting basin. On the left is the gate of the casting basin, which is lifted during float-out to float the pontoons into Grays Harbor.




View of a new Cycle 2 pontoon in progress with construction cranes in the background.

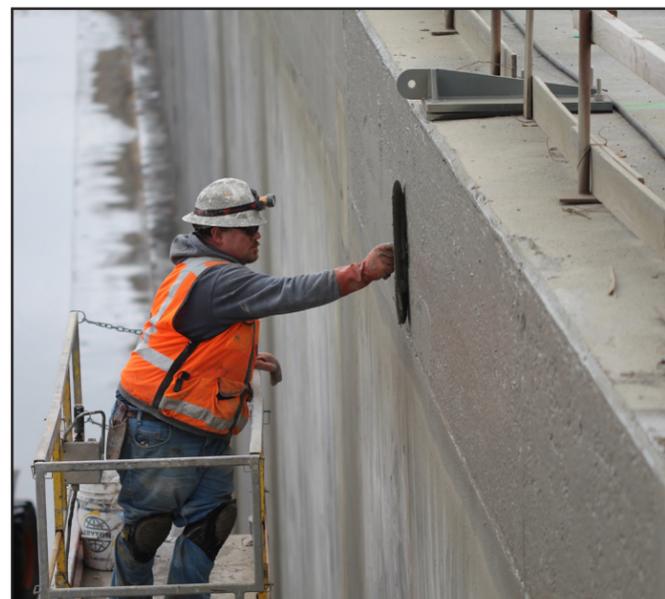

A pontoon construction worker applies grout to the exterior of a 360-foot-long longitudinal pontoon.


## Pontoon float-out - Aberdeen

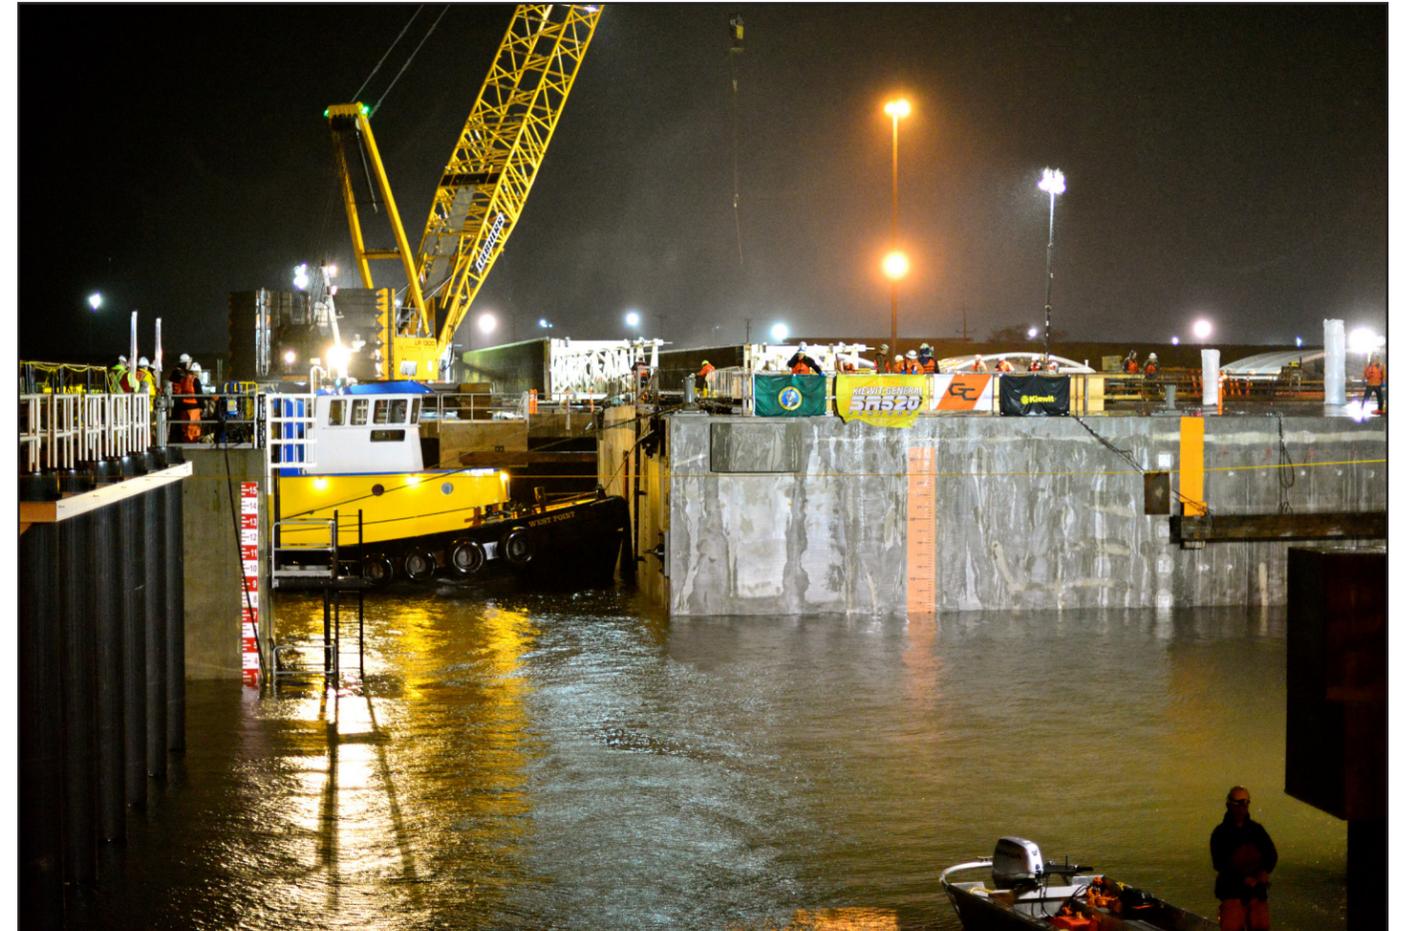

Pontoons were floated out of the casting basin shortly after the high tide on April 28, 2013. Once the basin was flooded and the gate was removed, crews brought in tugboats to remove the six Cycle 2 pontoons.



Crews used a crane to remove the gate of the casting basin, prior to floating the pontoons out.

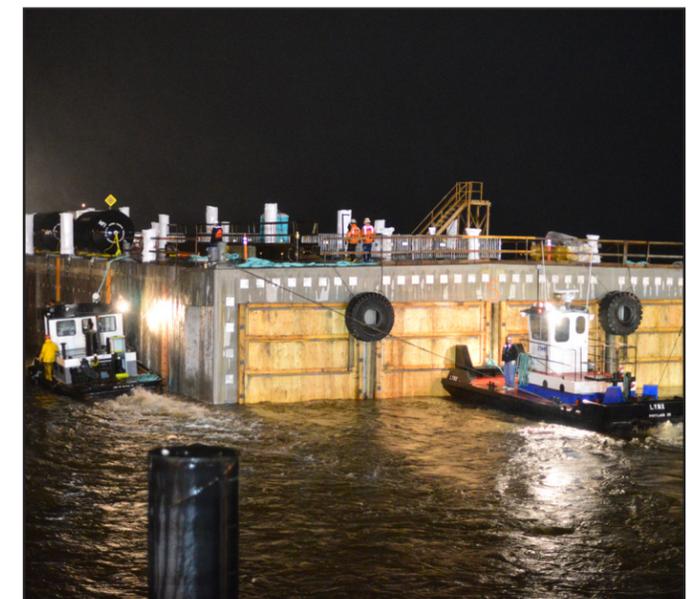

Crews used tug boats to guide the pontoons out of the basin and into Grays Harbor.
